


ID	Task Mode	Task Name	Duration	Start	Finish	Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr 4, 2025					
						Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct					
1		New Wastewater Treatment Plant Contract 4-LS & FM	330.88 days?	Wed 5/1/24	Fri 8/15/25																								
2		Award	1 day?	Wed 5/1/24	Wed 5/1/24																								
3		Execute Contract	19 days	Wed 5/1/24	Mon 5/27/24																								
4		Submittal Process	111 days?	Wed 5/29/24	Fri 11/1/24																								
5		Pre construction meeting	1 day?	Wed 6/12/24	Wed 6/12/24																								
6		River Road	201 days	Fri 11/1/24	Fri 8/15/25																								
7		SWPPP Installation/Mobilization	5 days	Fri 11/1/24	Thu 11/7/24																								
8		Remove and Replace Storm Sewer	2 days	Fri 11/8/24	Mon 11/11/24																								
9		Dewatering Installation	5 days	Tue 11/12/24	Mon 11/18/24																								
10		Over Excavate LS site to 943.00	5 days	Tue 11/19/24	Mon 11/25/24																								
11		Install Lift Station	6 days	Tue 11/26/24	Wed 12/4/24																								
12		Re-compact Mass Excavation	7 days	Thu 12/5/24	Fri 12/13/24																								
13		Site Grading/Fill Placement	8 days	Mon 12/16/24	Thu 12/26/24																								
14		8" SS between existing MHs	2 days	Mon 9/16/24	Tue 9/17/24																								
15		12" SS to Lift Station	3 days	Tue 1/7/25	Thu 1/9/25																								
16		Water Line	3 days	Fri 1/10/25	Tue 1/14/25																								
17		Valve Vault Installation	5 days	Wed 1/15/25	Tue 1/21/25																								
18		Process Piping	4 days	Wed 1/22/25	Mon 1/27/25																								
19		4" Force Main	5 days	Tue 1/28/25	Mon 2/3/25																								
20		Electrical	15 days	Tue 1/28/25	Mon 2/17/25																								
21		Gravel Surfacing and Paving	10 days	Tue 2/18/25	Mon 3/3/25																								
22		Seeding	2 days	Tue 3/4/25	Wed 3/5/25																								
23		Start-up	2 days	Thu 5/1/25	Fri 5/2/25																								
24		On The Green	145 days	Tue 11/5/24	Fri 5/30/25																								
25		Tree Removal	7 days	Tue 11/5/24	Wed 11/13/24																								
26		Site Grading	12 days	Tue 1/28/25	Wed 2/12/25																								
27		4" Force Main	8 days	Tue 2/4/25	Thu 2/13/25																								
28		Lift Station, Valve Vault & Meter Pit Installation	20 days	Thu 2/13/25	Wed 3/12/25																								
29		Pump Station Site Sanitary	5 days	Thu 3/13/25	Wed 3/19/25																								
30		Storm Sewer	5 days	Thu 3/20/25	Wed 3/26/25																								



ID	Task Mode	Task Name	Duration	Start	Finish	Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr 4, 2025
						Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
31		Water Line	3 days	Thu 3/27/25	Mon 3/31/25																			
32		Process Piping	6 days	Tue 4/1/25	Tue 4/8/25																			
33		Electrical	15 days	Tue 4/1/25	Mon 4/21/25																			
34		Ave G Sanitary	8 days	Wed 4/9/25	Fri 4/18/25																			
35		Ave G Concrete Replacement	2 days	Mon 4/21/25	Tue 4/22/25																			
36		Retaining Wall	10 days	Mon 4/21/25	Fri 5/2/25																			
37		Subdrains	2 days	Mon 5/5/25	Tue 5/6/25																			
38		Paving	10 days	Wed 5/7/25	Tue 5/20/25																			
39		Seeding & Lanscape Replacement	5 days	Wed 5/21/25	Wed 5/28/25																			
40		Start-up	2 days	Thu 5/29/25	Fri 5/30/25																			
41		Substantial Completion	0 days	Fri 7/25/25	Fri 7/25/25																			
42		Final Completion	0 days	Tue 9/30/25	Tue 9/30/25																			

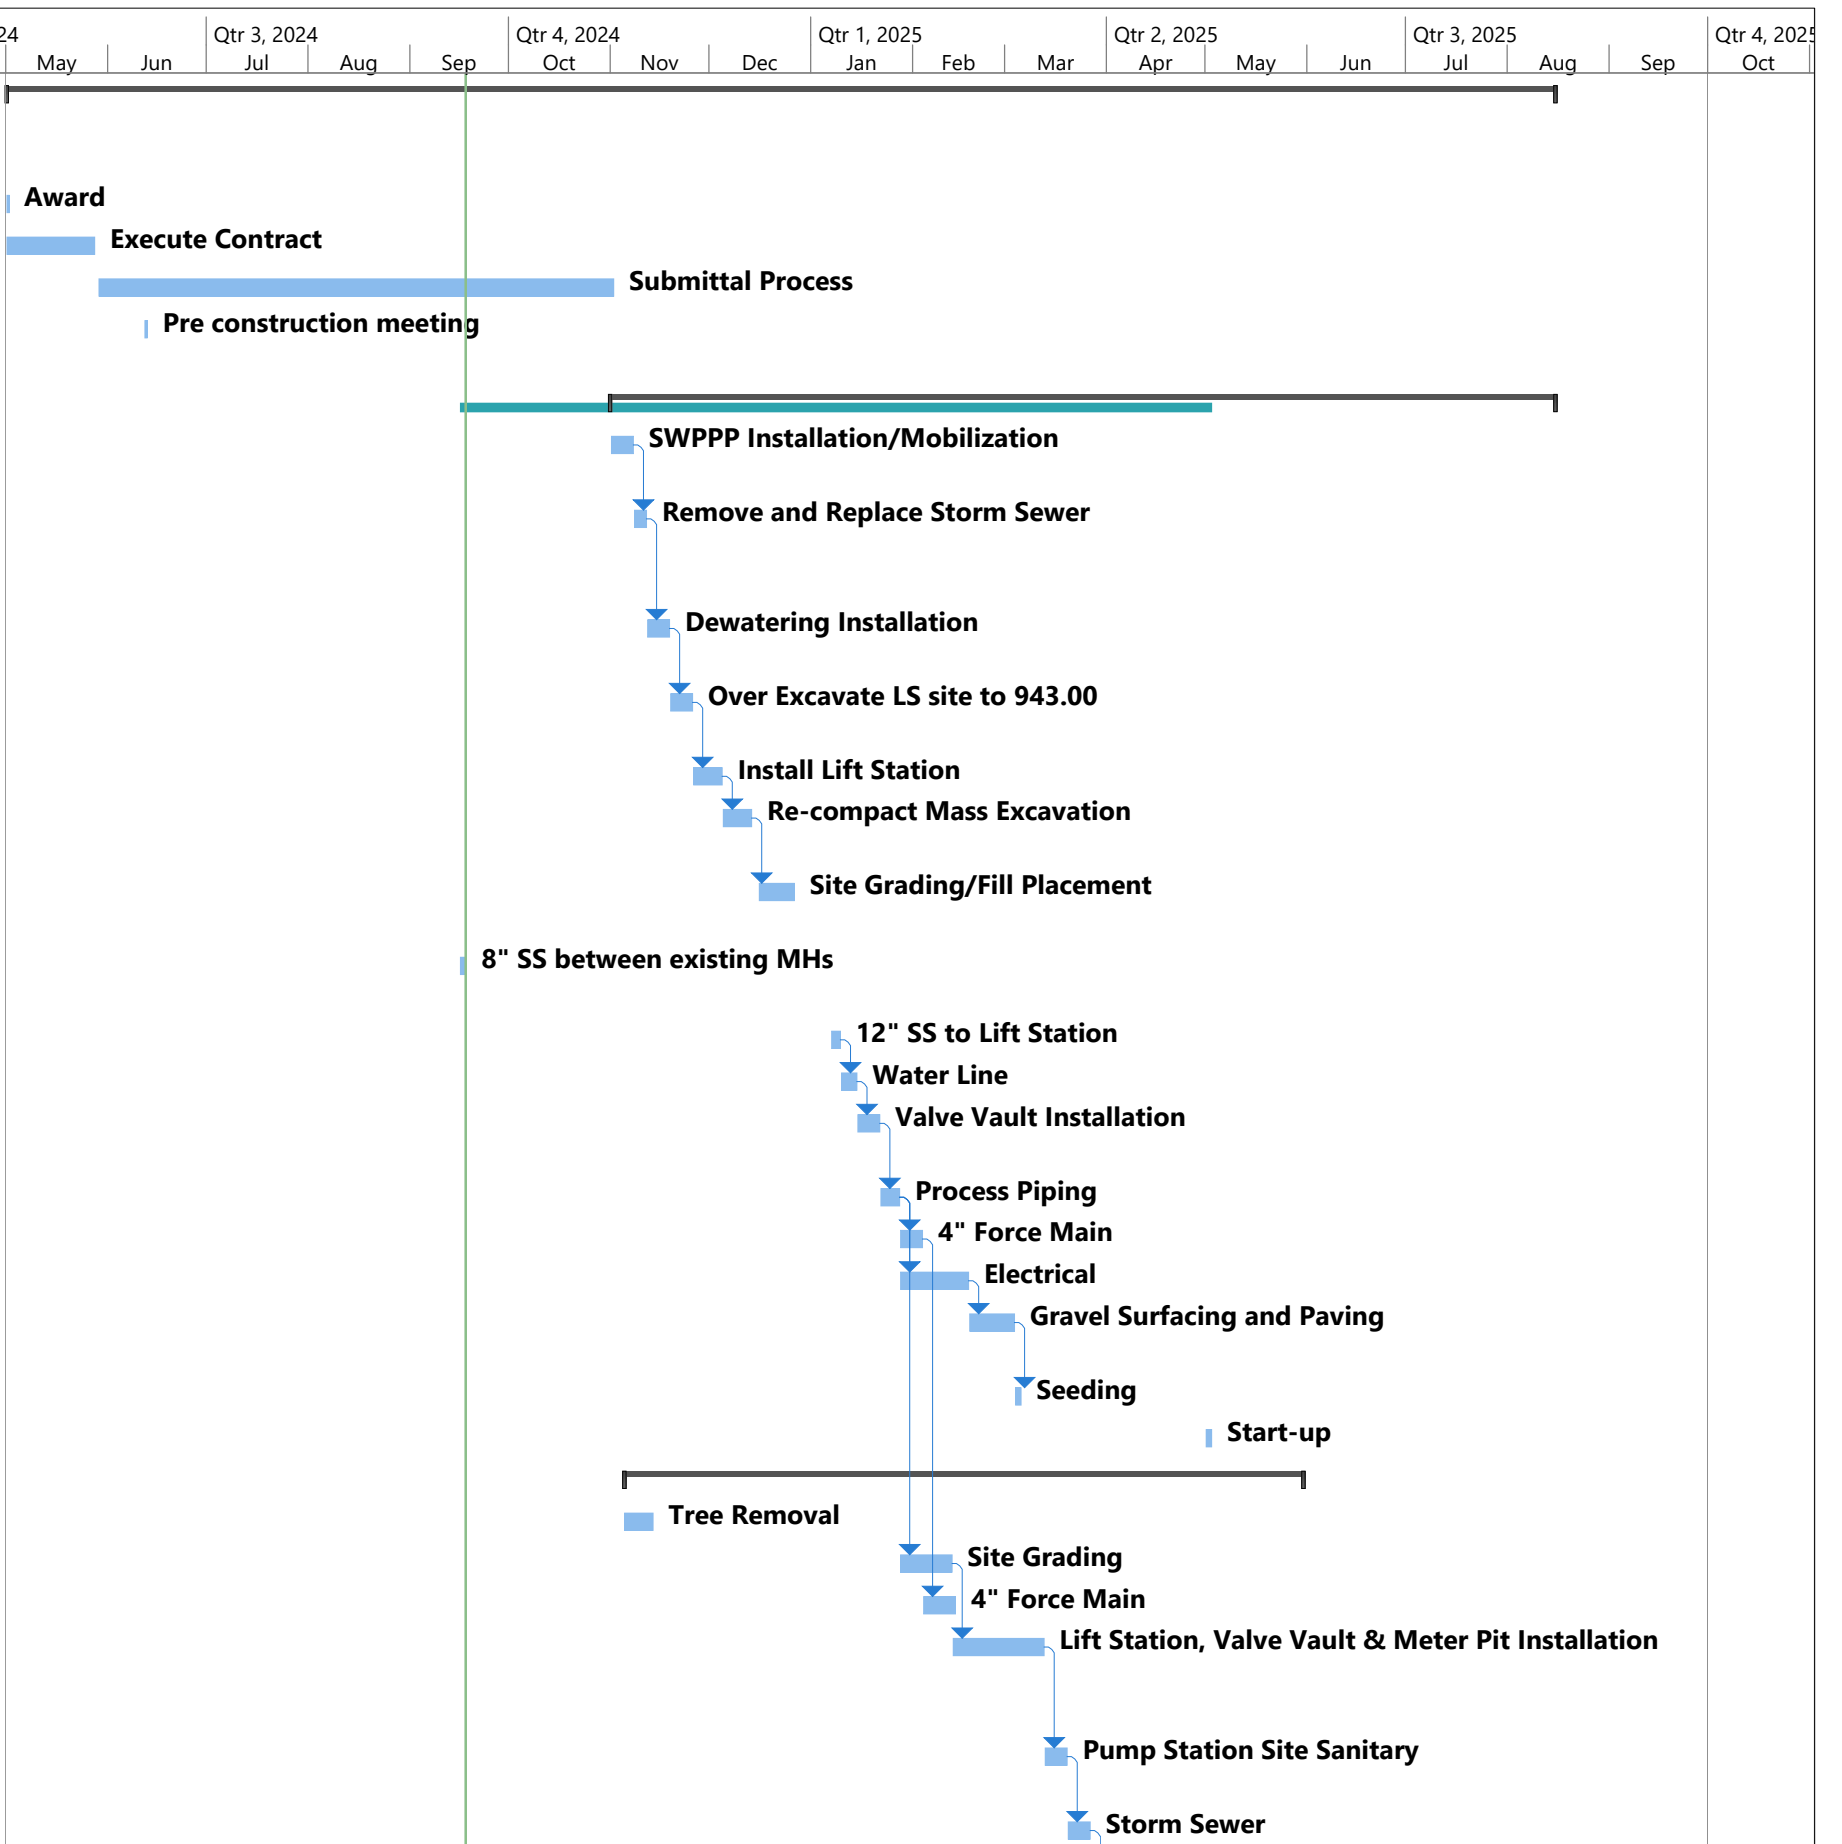
